

### COMPLETED WORKS


#### Geotechnical Investigations

During the last 5 months geotechnical investigations have taken place across the entire Lismore shire region. These works have involved using a drilling rig to understand subsurface conditions at the many landslip, bridge and culvert crossing locations. This information is vital in determining the most appropriate restoration design solution for these locations. All landslip, culvert and bridge geotechnical investigations have now been completed. We would like to thank residents for your patience and resilience during this time.

### CURRENT WORKS

#### Dorrroughby Road

The Dorroughby Road landslip restoration is well underway with embankment stabilisation completed last month. Drainage and road pavement works are scheduled to occur during March. See below progress photos, thanks to all the Dorroughby Road residents for your patience during this time.

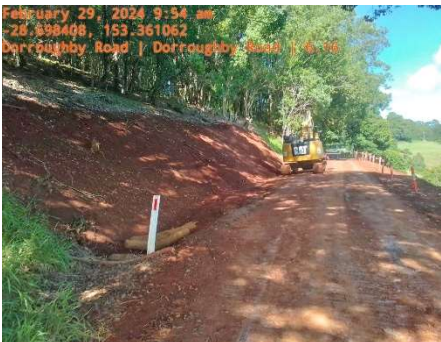

*Progress Works*

## Nimbin Road

Works are progressing on Nimbin Road at the site near Shipway Road. The retaining wall construction is now complete, and the road pavement works commenced end of February. Excitingly, traffic has temporarily moved onto the newly constructed northbound lane in preparation for an expected opening in April.



Nimbin Road – Site 4Km Works

## Guardrails Project

During the past month our guardrails project has been underway, replacing or installing new guardrails. This is multisite works to repair traffic barriers at road sections damaged during the 2022 natural disaster. Generally, the sites are at road sections over creek crossings. Each work site will require traffic control and the repair will generally be completed within 2 days. Recently, guardrails were completed for two sites at Nimbin Road, Rock Valley Road, Cawongla Road, Corndale Road and two sites at Boatharbour Road. Other road closures will be updated as scheduled work on Live Traffic.



Cawongla Road



Cawongla Road



Nimbin Road



Rock Valley Road



Rock Valley Road

## Tunable Creek Road

Works are currently underway on Tuntable Creek Road near Young Road. These involve reshaping of table drains, slashing and minor landslip remediation from Young Road heading back down the hill approximately 500m. The works are expected to be completed first week of March, pending weather conditions.

### Terania Creek – Bridge Updates

The Terania Creek bridge project is underway for bridge 1, 2 and 3. The bridge approaches and guard rail footings are completed for bridge 1 and bridge 2. During early March, work crews will commence final concrete works and installation of lateral restrain brackets for bridge 3.

### Newton Drive

A number of minor up slope landslips and a single pipe culvert were scheduled to be repaired during February, these works have now been pushed into March due to weather delays. Works will involve scaling of boulders and the clearing and reformation of a table drain to return the road to pre-existing condition. Works will be completed under traffic control and will have minimal impact on the residents in this area.

### Rosebank Road

Landslip restoration works were scheduled for completed during February; these works have now been pushed into March due to weather delays. The works involve reinstating the property access track and restoring the batter and table drain along the road edge. Works will be completed under traffic control and will have minimal impact on the residents.

### Industry Drive

Works have commenced on Industry Drive to improve drainage works involving the construction of a gabion wall to prevent future erosion. The works will occur for approximately two weeks, from Thursday 29 February, pending weather conditions. For further information, please view the original notice at

[https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news\\_feed/industry-drive](https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/industry-drive)



*Industry Drive*

### Rogerson Road

The team have been busy implementing appropriate protocols to ensure the safety of juvenile micro bats. Through successful collaboration with environmental professionals this protected species will be temporary relocated. This will allow the pups to complete their growth cycle during the breeding season and reduce their risk in maturing. Works are scheduled to recommence in late March. For further information, please view the original notice at:

[https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news\\_feed/rogerson-road-culvert-replacement-feb-2024](https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/rogerson-road-culvert-replacement-feb-2024)



## **FUTURE WORKS**

### **Johnston Road**

Works will commence to replace a damaged culvert headwall on Johnston Road for approximately two weeks, from 4 March to 18 March 2024, subject to weather conditions. The road will remain open under stop/go traffic control with slight delays expected. For further information, please view the original notice at

[https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news\\_feed/johnston-road-culvert-works-feb-2023](https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/johnston-road-culvert-works-feb-2023)

### **Eureka Road, Graham Road & Haywood Lane**

During the end of February, all three bridges were successfully delivered to Council storage yards. The designs for each site are in the final stages with works schedules being finalised. We apologise in advance for any disruptions you may experience while we carry out this essential work. These works will involve removing the existing infrastructure at each site and preparing the area for bridge construction. To minimise impact to residents and traffic flow during the construction work a temporary track will be established as a side road. The work duration at each site is expected to be approximately 6 weeks, subject to weather conditions.



*Bridges Delivered to storage yard*

### **Blue Knob Road**

Remediation works are planned to commence in April 2024 on several landslips on Blue Knob Road, the two sites currently under temporary traffic control measures. Our primary focus is to ensure the well-being of our community and to efficiently manage the project to minimise disruption. We will notify residents of the exact date and provide further information on the works closer to commencement. The expected duration of the works will be approximately nine months, this estimated period includes the remediation of the total of four landslips.



*Damaged Sites*

### **Leycester Road**

Leycester Road design is currently underway with expected completion in May 2024. Works are expected to start on site in August 2024 and will take approximately two months to complete. Funding for these works has been approved.

### **Oakey Creek Road**

Currently there are five major landslips on Oakey Creek Road. Due to the complex nature of these sites, which involves multiple design iterations and reviews from civil, structural, and geotechnical engineers, the designs are expected to be completed by September 2024, with works to commence early in 2025 pending funding approvals.

### **Stony Chute Road**

There are multiple landslips along Stony Chute Road, seven of these being complex and two being non-complex. Works will commence on the noncomplex sites during April with the expected completion of June 2024. The more complex sites are currently under design with this process anticipated to be completed by August 2024 and works estimated to start towards the end of 2024 pending funding approvals.

### **Terania Creek Road**

Terania creek Road has multiple landslip sites currently under design with expected completion in September 2024 with works estimated to commence in early 2025 pending funding approval. Currently works are underway on multiple bridges with works anticipated to be completed mid-2024.

### **Wallace Road**

Wallace road has two major landslips currently under design with this process expected to be completed by the end of June 2024. It is estimated the works will commence towards the end of 2024 pending funding approvals. Please note, we are unable to schedule works until we receive funding approval.

### **Woodlawn Road**

Woodlawn Road design is currently underway with expected completion in May 2024. Works are estimated to start on site in August 2024 and will take approximately three months to complete. Funding for these works has been approved.
