

### CURRENT WORKS

#### Blue Knob Road


Progress on the Blue Knob Road landslip project is progressing well. The soil nail installation at the first site is complete and shotcrete works will commence shortly. Drilling is underway at Site 2 and 3 with soil nailing started at end of the month and expected to continue throughout September.



*Blue Knob Road*

#### Eureka Road


Road and bridge reconstruction is now completed. Minor damage from the 12 August 24 rainfall event caused some damage on the new pavements which is being repaired in September.

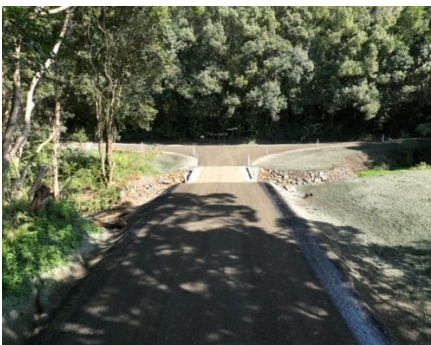

*Eureka Road*

#### Graham Road

New bridge and road reconstruction works were completed on time by late August 2024. The road has reopened to traffic without restrictions.

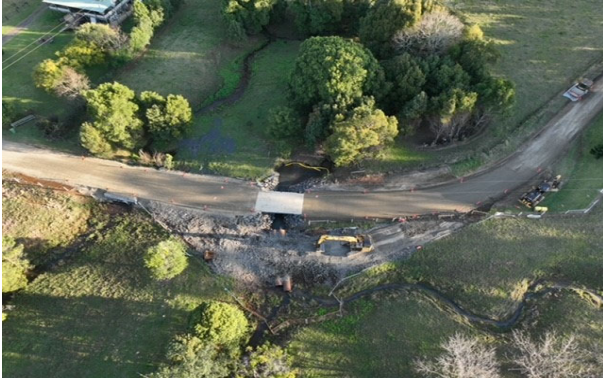

*Graham Road*

### **Haywood Lane**

New bridge and road reconstruction works were completed on time by late August 2024. The road has reopened to traffic without restrictions.



*Haywood Lane*

### **Leycester Road**

Leycester Road is approximately 25-percent completed with table drains, bulk earthworks and stormwater pipelaying ongoing. Works are expected to be completed by end of November, 24.



*Leycester Road*

## Newton Drive

Slip remediation and road reconstruction works were completed by late August 2024. The road has reopened to traffic without restrictions.



*Newton Drive*

## Gravel Roads – Multiple Sites


Works continue to grade more than 150 kilometres of unsealed, gravel roads which suffered substantial damage due to additional declared natural disasters in December 2023 and April 2024. Lismore City Council has six dedicated work crews, strategically deployed to optimise efficiency and resource allocation. Recently completed roads include Terania Creek Road, Young Road, Fairfull Road, Izzard Road, Monaltrie Road, Anderson Road, Munro Road, Cross Road, Eastment Lane.



*Monaltrie Road – Grading Works*



*Cross Road – grading works*

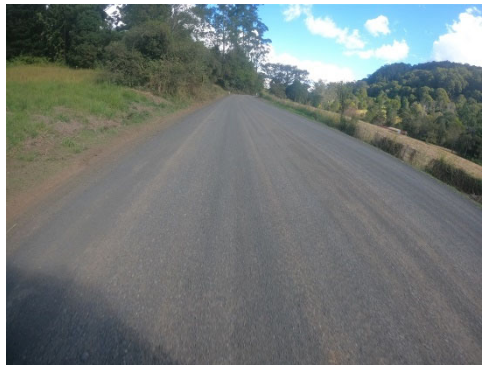

*Terania Creek Road – Grading works*

## Repentance Creek Road

Restoration works on Repentance Creek Road commenced in late August 24 and are expected to continue until completion around mid-October 24, subject to weather conditions.

The 8-week project includes drains, bulk earthworks and road reconstruction works, and some road pavement works.

The road remains open, with works continuing under stop/go traffic control, some short delays are expected.

For more details visit: [https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news\\_feed/works-notice-repentance-creek-road-jul-2024](https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/works-notice-repentance-creek-road-jul-2024)

## Rogerson Road

Road reconstruction works - including the creation and installation of two customised headwalls - are now completed at Rogerson Road and the road has reopened to traffic without restrictions. Lismore's Flood Restoration Portfolio would like to thank residents and visitors for their patience as we carried out this complex restoration project, which included rehousing 7 southern myotis bats into a specially constructed 'bat box' made by Rob of the Flood Restoration Portfolio. In a delicate operation, the bat box (pictured) was returned to the sanctuary of the concrete archway for the bats to find shelter and safety.



*Rogerson Road*

### **Stony Chute Road**

Earthworks are now completed, and site rehabilitation is underway. The drainage works will be completed by mid September, with the final pavement works to follow. Motorists can expect some short delays at the site with stop/go traffic controls in operation. The project is scheduled for completion at the end of September.



## Stony Chute Road

### Terania Creek Road

Restoration works continue at Bridge 1 following the recent installation of a side track for vehicle access through the works site.

Bridges 2 and 3 have been restored with guard rail installation now complete. Motorists are advised to approach the continuing works site with care.



*Terania Creek Road – Bridge 2*



*Terania Creek Road – Bridge 3 Completed*



## FUTURE WORKS

### Urban Drainage

The Urban Drain Cleaning Program continues on Barnes Ave, Caniaba Street, Casino Street, Cromer Street, Engine Street & Kyogle Street.

### Gwynne Road

Tender is due 5 September 24 and will be awarded approx. 3 weeks from then. Restoration works should start early October 24.

### Branch Creek Bridge

Design complete.

Procurement underway with supply of pre-stressed bridge beams awarded and piling RFQ being evaluated.

Construction scheduled to commence September 24.

### Paterson Bridge

Design underway with IFC plans expected end July.

Procurement activities to follow.

Construction currently scheduled for March 25

### Cosy Camp Road

Design Complete.

Procurement activities underway.

Construction currently scheduled to start end Sept 24

Works involves road widening and guardrail installation

### **Stanger Road**

Design Complete.

Procurement activities underway.

Construction currently scheduled to start mid Oct 24

Works involves road widening and guardrail installation

### **Skyline Road**

Design Complete.

Procurement activities underway.

Construction currently scheduled to start early Nov 24

Works involves horizontal drainage instalation and pavement reconstruction
