

COMPLETED WORKS

Flood Restoration – Roads & Bridges Program

Gravel Roads Program – Multiple Sites

Throughout December, several roads were completed within the gravel roads program. Grading and drainage restoration works were completed for Ashlin Rd and Fox Rd. Furthermore, emergency grading and drainage works were completed on Boundary Crk Rd, Bentley Rd, Blade Rd, Chelmsford Rd, Cordyline Rd, Emerson Rd, Lindsay Rd, Maso Rd, Quilty Rd, Starkey Rd, Suffolk Rd, and Robb Rd with emergency temporary culvert repairs also completed on Wyrallah Rd. We thank the community for their patience as we continue through this extensive schedule of works.



Maso Rd



Ashlin Rd



Fox Rd

Flood Restoration – Buildings Program

Miscellaneous Grants Works

- **Sam Trimble Oval (Brick Building Refurbishment):** Completed and handed back to the community.
- **Riverside Park Toilets:** Epoxy floors and plumbing electrical fit-off completed.



Riverside Park Toilets

Flood Restoration – Flood Resilience Program

Urban Drain Cleaning Program

The Urban Drains Cleaning Program was completed in December with the remaining areas approved in the scope of works cleaned.

CURRENT WORKS

Flood Restoration – Roads & Bridges Program

Blue Knob Road (Site DM00680)

The contractor, CMC, has completed the shotcrete placement and no-fines concrete backfilling. Following the Christmas break, CMC will commence preparations for the guardrail footing pour.



Blue Knob Road (Site DM00680)

Blue Knob Road (Site DM01366)

The CMC subcontractor has completed the additional acceptance testing required by geotechnical contractor, GHD. However, due to heavy rainfall and drilling contractor unavailability, installation of additional soil nails was postponed until 2025. To prevent collapses during the Christmas break, CMC covered the excavation with plastic sheeting.



Blue Knob Road (Site DM01366)

Blue Knob Road (Site DM01361/DM01449)

The CMC subcontractor has successfully completed the installation of all soil nails and the necessary acceptance tests. Furthermore, CMC has partially installed the no-fines concrete backfill and placed the galvanised mesh, in preparation for the first lift of the final shotcrete layer on walls 3 and 4 following the Christmas break.



Blue Knob Road (Site DM01361/DM01449)

Gravel Roads Program (Multiple Sites)

Works continue for grading over 150 kms of unsealed gravel roads. Current and upcoming works include Armstrong Rd, Beacombs Rd, Lychee Rd, and Nightcap Range Rd.

Gwynne Road

Works are progressing on Gwynne Road; however, the works have been extended and will continue to the end of March.

Leycester Road

Works are nearing completion, with the pavement stabilisation and bituminous sealing successfully finished this week. Some minor finishing will continue in early 2025.



Leycester Road

Repentance Creek Road

Pavement stabilisation and bituminous sealing works were completed during December with the project continuing finishing works in the new year, progressing towards completion.



Repentance Creek Road

Rural Drain Cleaning Program

Last month, our contractor, HXR was busy cleaning out and flushing stormwater pipes for Boyle Rd, Bishop Creek Rd, Sibley St, Anderson Rd, Gungas Rd, Blue Knob Rd, Emerson Rd, Coopers Creek Rd and Frasers Rd.

Terania Creek Road (Branch Creek Bridge)

In December, significant progress was made, key accomplishments included the backfilling of abutments, installation of bearing pads, successful landing of pre-stressed concrete beams, and the completion of the concrete bridge deck, which involved forming up, steel tying, and pouring. Looking ahead to January and February, the project will focus on finalising the construction of new bridge approach works and demolishing the existing causeway structure. Additional tasks scheduled include bitumen sealing of the approaches, road furniture installation, and site de-establishment. These upcoming works will mark the projects final stages, bringing it closer to completion.



Branch Creek Bridge

Tunable Creek Road (DM01136)

Pavement stabilisation and bituminous sealing works were completed during December with the project continuing finishing works in the new year, progressing towards completion.

Woodlawn Road

The temporary sidetrack is now 80% complete and weather permitting, traffic will be diverted onto the temporary road mid-Jan to facilitate the landslip remediation and pavement failure, which is expected to take approximately five months.




Woodlawn Road

Flood Restoration – Buildings Program

Lismore Library


Excitingly, the finishing touches are underway at the library this month. Level 1 furniture is in ready with shelving and signage in place. Meanwhile, on level 2 the flooring is in proceeding on schedule for the project.

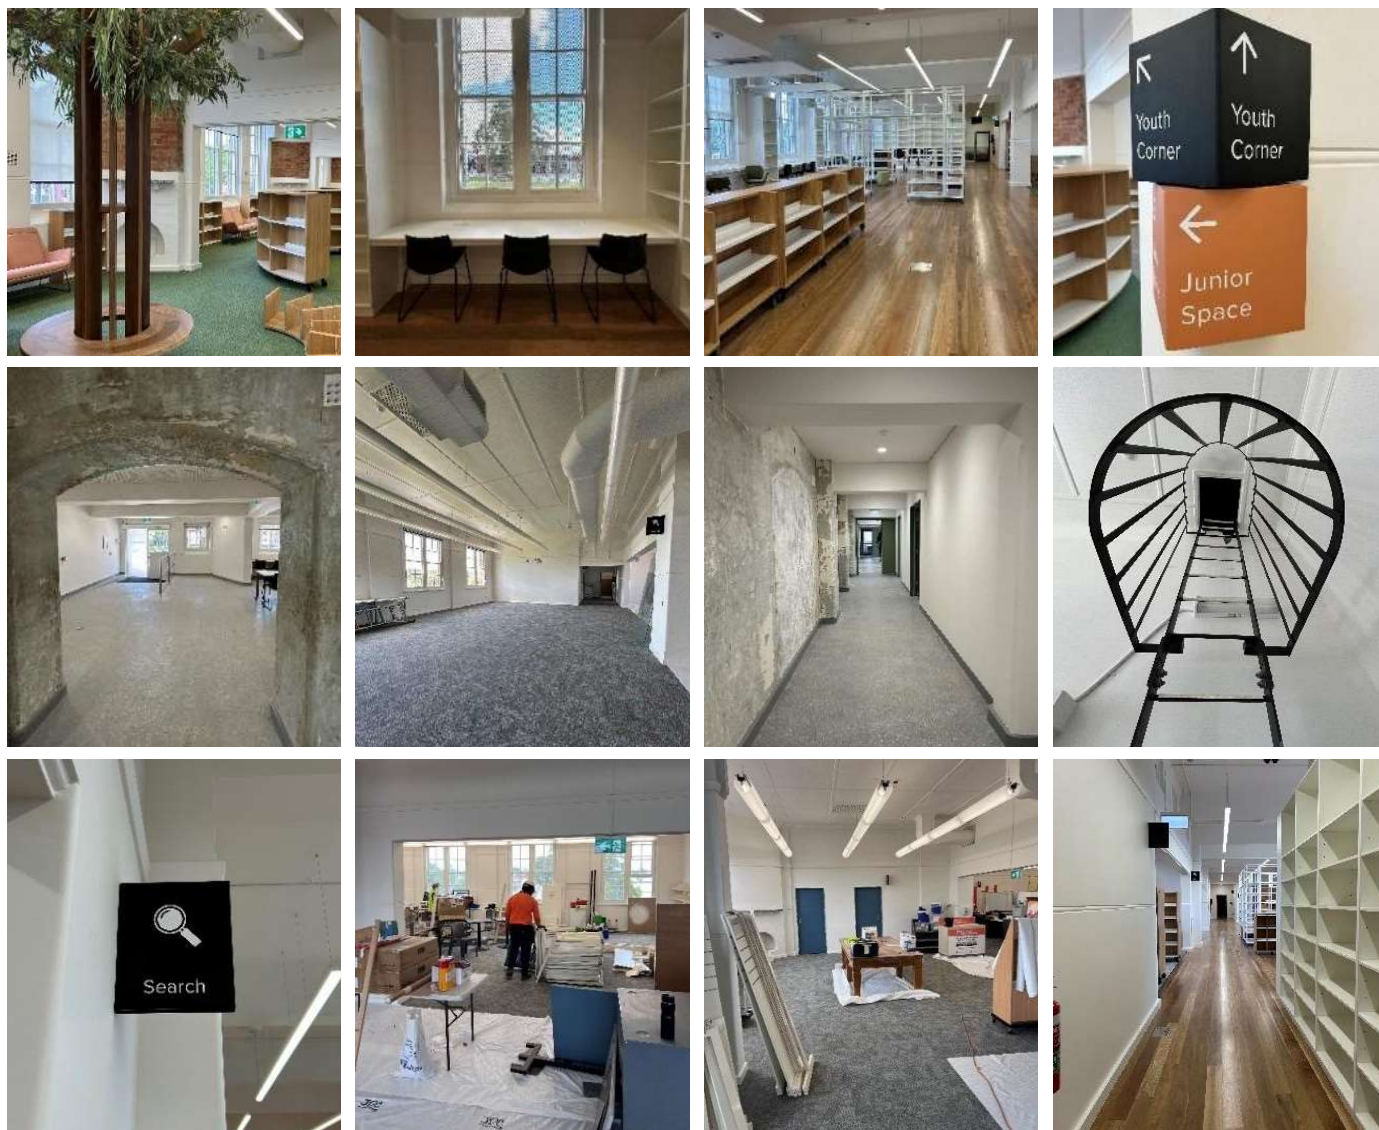

Lismore Library

Lismore Municipal Building

The site was a hive of activity in December. Final touches were underway with furniture moved back to the main room to allow finalisation of the front rooms. The vinyl flooring is nearing completion with only some edging work remaining.

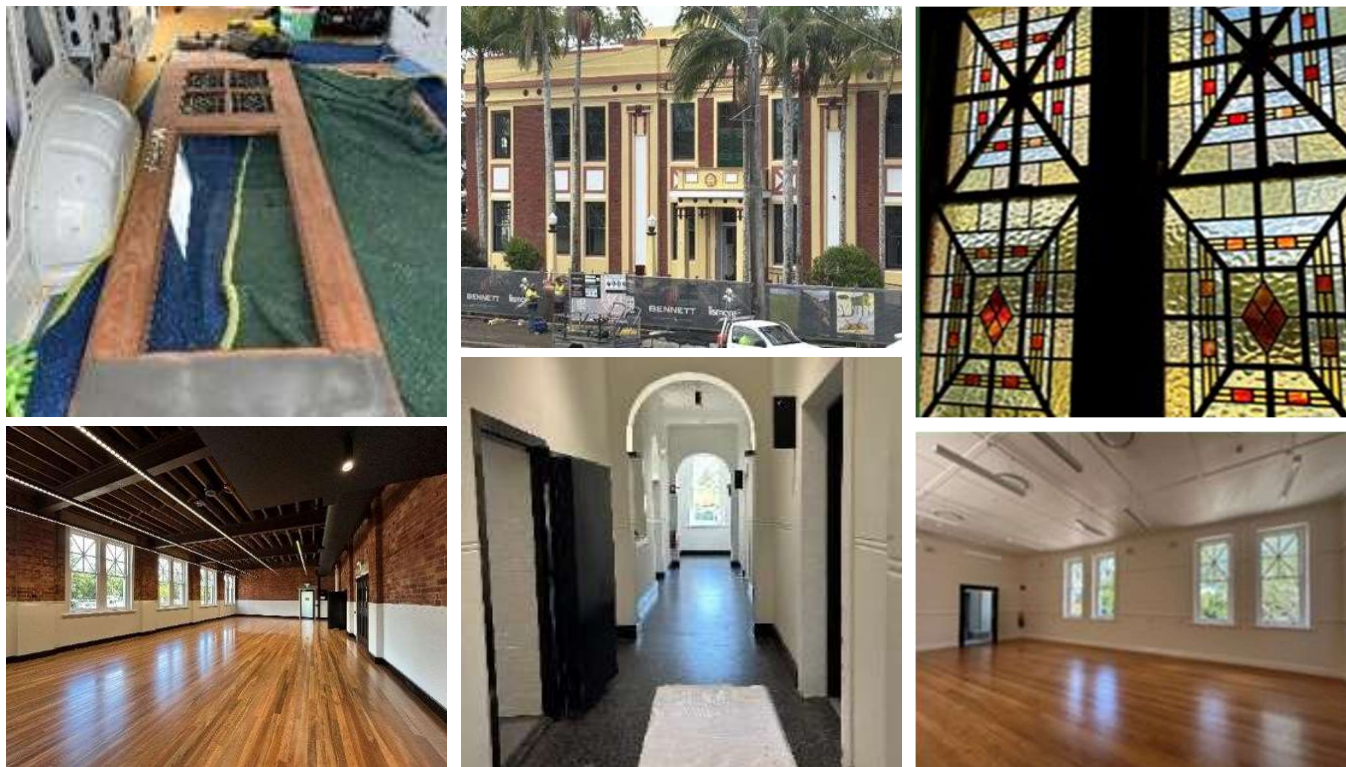

Lismore Municipal Building

Public Amenities Buildings

- **Nesbitt Park:** Slab poured 4th December
- **Neilson Park (Cricket):** Slab poured 27th November
- **Riverview Park Amenities:** Slabs complete awaiting modular building delivery
- **Albert Park Amenities:** Slabs complete awaiting modular building delivery
- **Sam Trimble Oval Amenities:** Slabs complete awaiting modular building delivery
- **McKenzie Park Amenities:** Slabs complete awaiting modular building delivery
- **Neilson Park:** Slabs complete awaiting modular building delivery



Miscellaneous Grants Works

- **Nimbin Toilet Block:** Underway – Site visit with electrical contractor to discuss scope.

Visitor Information Centre

New slab hydraulics are installed and new slabs footings excavated ready for concrete pour. Internal hydraulics installation almost complete.



Visitor Information Centre

Flood Restoration – Water & Waste Program

Lismore Waste Facility (Landfill Cell 2B)

In response to the 2022 flood event, comprehensive onsite investigations have been initiated to evaluate the extent of damage incurred. These activities involve the removal of landfill media to expose underlying containment systems, enabling engineering teams to conduct thorough examinations and determine the scope of necessary replacements and repairs. Concurrent with these efforts, stormwater divergence works are currently in progress. Additionally, GeoTech Cone Penetration Testing (CPT) drilling is scheduled to commence in January, focusing on assessing the integrity of bund walls. These multifaceted approaches aim to provide a holistic understanding of the site's condition and inform subsequent remediation strategies.

FUTURE WORKS

Flood Restoration – Roads & Bridges Program

Skyline Road

Works are planned to commence in January on Skyline Road to construct horizontal borehole drains and undertake pavement repairs.

Stanger Road

Road realignment works and guardrail installation are scheduled to commence in February.

If you would like to be added to a notification list for a specific region, please visit the below website page and completed the notification form to register your contact details to receive Flood Restoration Portfolio works updates.

<https://www.lismore.nsw.gov.au/Business/Flood-Restoration-Portfolio/FRP-Project-Updates>
