

COMPLETED WORKS

Tunable Falls Road

Temporary sealed patching works were recently completed for Tuntable Falls Road. These works involved placing overlay, stabilise, trim and sealing the road surface height to repair damages from the 2022 flooding event.



Tunable Falls Road aerial view of works



Tunable Falls Road aerial view of works



Tunable Falls Road aerial view of works

Tunable Creek Road

After establishing a baseline for the monitoring process and developing a management plan, the temporary track opened on Tuesday, the 14th of March. Due to the volatile nature of the landslip and risks of further damages occurring a detailed risk assessment was undertaken to control access until a permanent solution is implemented. The risk assessment requires weekly visual monitoring, survey monitoring of fixed control points and monthly inspections by a geotechnical engineer. Restrictions will be placed on the temporary access road during large rain events to mitigate risks to public. Should the road be closed due to adverse weather, VMS boards placed at The Channon and Nimbin will identify the road closure. Facebook updates will also communicate the closure to the wider community. Please report hazards or changes to Lismore City Council using reference LCC92.



Tunable Creek Road temporary track



Tunable Creek Road works aerial view



Tunable Creek Road during works

CURRENT WORKS

Mackie Road

The Mackie Road culvert to bridge replacement at Johnston Creek, works are currently underway after starting on Monday the 13th of March. The project works will operate for approximately three months with a planned completion in late June 2023, subject to fine weather. Due to the nature of the works a full 24-hour hard road closure is required during the March – June 2023 works period around the site location. For further details and to view a map of the works, please visit the Mackie Road bridge update link below:

https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/mackie-road-bridge-feb-2023



Mackie Road Bridge being delivered to the bridge storage yard



Mackie Road Bridge during construction

Wyrallah Road

Pavement rehabilitation works started at the end of January to reconstruct and rehabilitate approximately 500m of Wyrallah Road. Throughout this construction process drainage works, kerb installation and subsoil installation will also be completed. The site closed on the 24th of March, with recommencement expected mid-April to allow for required drainage re-design and survey prior to finalising the section and switching traffic and commencing the Northbound Lane. For further details please visit the Wyrallah Road update link below:

https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/wyrallah-road-jan-2023



Wyrallah Road / Emily Street during works



Wyrallah Road / Emily Street during works



Wyrallah Road / Emily Street during works



Wyrallah Road / Emily Street during works



Wyrallah Road / Emily Street during works



Wyrallah Road / Emily Street during works

Crofton Road

All drainage and pipe work is scheduled to be completed by Thursday the 6th of April. These works include desilt and reshape table drainage, installing headwalls and pipe extensions as required to ensure water runoff from the road, to prevent future road damages from occurring.



Crofton Road pipe installation works



Crofton Road pipe installation works



Crofton Road pipe installation works



Crofton Road pipe installation works



Crofton Road pipe installation works


Quilty Road

The remaining drainage works are scheduled to commence after Easter for Quilty Road.

FUTURE WORKS

Town Road

Funding through the Fixing Country Bridges program has been awarded to replace the damaged structure with a new bridge. The bridge superstructure is currently being constructed in France with an innovative steel beam that will be launched into place in one piece. A unique type of structure, this bridge will be the first in the region. A general plan of the works is provided below. The Town Road bridge superstructure will be delivered at the end of May 2023. Civil works are scheduled to begin in April 2023 with a planned completion in late July 2023, subject to fine weather. Further updates will be provided towards the end of March 2023.

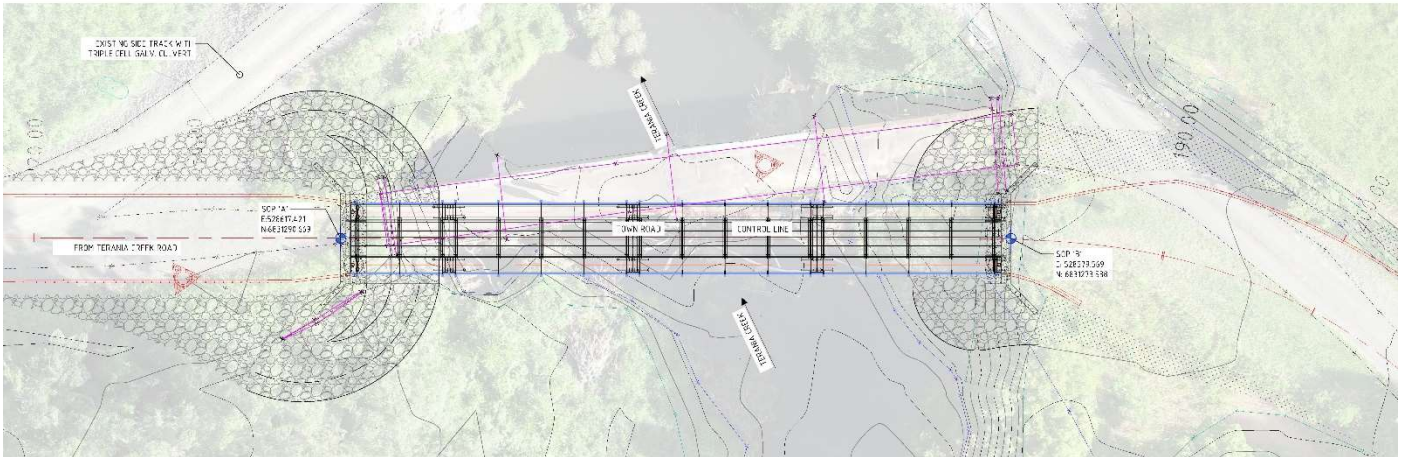

Town Road Bridge General Arrangement Plan Scaled 1:125
