

**Roads and Bridges Flood Restoration Works Update – 12th December 2022**

**CURRENT WORKS – SEALED ROADS**

**Riverbank Road**

To repair the issues caused from the February and March 2022 floods, restoration works have been performed on Riverbank Road. These involved overlay, stabilise, trim and seal road surface to repair damages.



*Image: Riverbank Road flood damage*

**Jiggi Road**

Likewise, Jiggi Road has undergone recent works to address issues caused from the February and March 2022 floods. This has involved overlay, stabilise, trim and seal road surface to repair damages.



*Image: Jiggi Road flood damage*

## CURRENT WORKS – UNSEALED ROADS

### **Braidwood Road**

Braidwood Road has recently had unsealed road works completed, the below image outlines the after result for the road.



*Image: Braidwood Road completed works*

### **Ashlin Road**


Ashlin Road recently underwent repair works, these are now completed. The image below shows the before image of the roads condition.



*Image: Ashlin Road before works*

### **Leeson Road**

Unsealed road works were recently completed for Leeson Road. The below image outlines the before condition of the road.

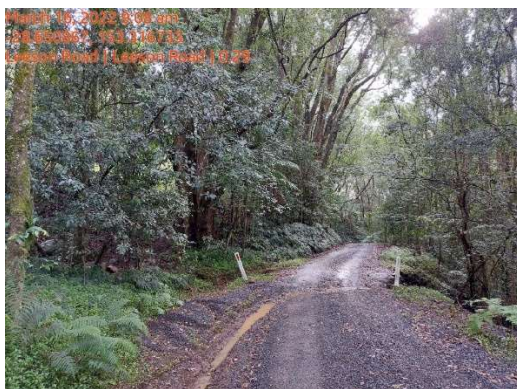

*Image: Leeson Road before works*

## Upper Tuntable Falls Road

Repair work was recently carried out and are now completed for Upper Tuntable Falls Road. The image below shows the before image of the roads condition.



Image: Upper Tuntable Falls Road before works

## CURRENT WORKS – EMERGENCY ROAD REPAIRS

### Tatham Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. A planned return is scheduled for 2023 to complete permanent works.



Image: Tatham Road before works

### Tucki Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. A planned return is scheduled for 2023 to complete permanent works.



Image: Tucki Road before works

## CURRENT WORKS – DRAINAGE WORKS

### Keerrong Road

Desilt and reshape table drainage, while installing headwalls and pipe extensions as required to ensure water runoff from the road, to prevent future road damages from occurring.



Image: Keerrong Road

## FUTURE WORKS – SEALED ROADS

### Corndale Road

Replace existing road surface, stabilise, trim and seal of existing road surface to repair damages from the February and March, 2022 floods.



Image: Corndale Road

### Keerrong Road

Overlay, stabilise, trim and seal road surface to repair damages from the February and March, 2022 floods.



Image: Keerrong Road

## FUTURE WORKS – UNSEALED ROADS

### East Road, Mountain Top Road, Terania Creek Road & Wallace Road

Planning is in place to perform works shortly on the following unsealed roads: Terania Creek Road (Section before the landslip), Wallace Road, Mountain Top Road, and East Road.

## FUTURE WORKS – EMERGENCY ROAD REPAIRS

### Tunable Creek Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. A planned return is scheduled for 2023 to complete permanent works.



Image: Tuntable Creek Road

### Leycester Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. With a planned return to complete permanent works in 2023.



Image: Leycester Road before works


### Keerrong Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. With a planned return to complete permanent works in 2023.

## COMPLETED WORKS – SEALED & UNSEALED ROADS

### Jiggi Road

Works have been completed on Jiggi Road to address issues caused from the February and March 2022 floods. This has involved overlay, stabilise, trim and seal road surface to repair flood damages.

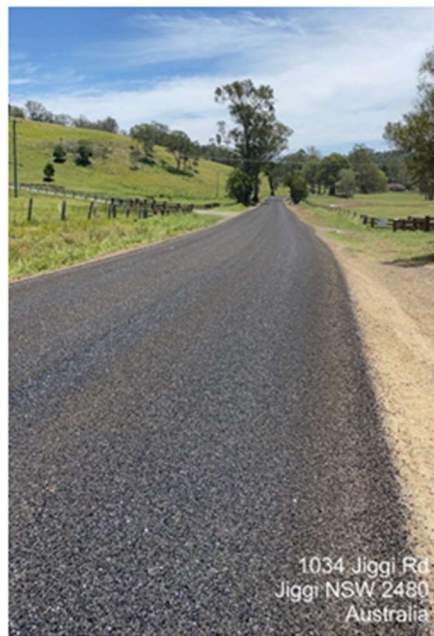

*Image: Jiggi Road before and after images*

### Ashlin Road

Overlay and drainage works are now completed on Ashlin Road to repair damages caused from the February and March 2022 floods.



*Image: Ashlin Road before and after images*

### Leeson Road

Overlay and drainage works are now completed on Leeson Road to repair damages caused from the February and March 2022 floods.



Image: Leeson Road before and after images

### Upper Tuntable Falls Road

Repair work was recently carried out for Upper Tuntable Falls Road. Overlay and drainage works are now completed to restore damages caused from the February and March 2022 floods.



Image: Upper Tuntable Falls Road before and after images

### Wallace Road

Wallace Road has recently undergone repair work up to the landslip. Overlay and drainage works are now completed to restore damages caused from the February and March 2022 floods.



Image: Wallace Road before and after images

## COMPLETED WORKS – EMERGENCY ROAD REPAIRS

### Tatham Road

Works were completed on Tatham Road to remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. A planned return is scheduled for 2023 to complete permanent works.



*Image: Tatham Road before and after images*

### **Tucki Road**

Tucki Road works have removed and replaced existing material from the road surface, graded and rolled the road with a temporary seal over the new surface. A planned return is scheduled for 2023 to complete permanent works.



*Image: Tucki Road before works image*



## CURRENT WORKS – SEALED ROADS

### Riverbank Road

Works are continuing for Riverbank Road to repair the issues caused from the February and March 2022 floods, restoration works have been performed on Riverbank Road. These involved overlay, stabilise, trim and seal road surface to repair flood damages.



Image: Riverbank Road before and after

## CURRENT WORKS – UNSEALED ROADS

### Corndale Road

Corndale Road continues to undergo works to replace existing road surface, stabilise, trim and seal of existing road surface height to repair damages from the February and March 2022 floods.



Image: Corndale Road before and after images

### East Road

Overlay and drainage works are currently being carried out on East Road to restore damages caused from the February and March 2022 floods.



Image: East Road before and after images

### Terania Creek Road

Work is currently underway between The Channon and Lawler Road on Terania Creek Road due to a landslip after Lawler Road. Overlay and drainage work are underway to repair damages caused from the February and March 2022 floods.



Image: Terania Creek Road before and after images

## CURRENT WORKS – EMERGENCY ROAD REPAIRS

### Keerrong Road

Works are continuing along Keerrong Road to overlay, stabilise, trim and seal road surface to repair damages from the February and March, 2022 floods.



Image: Keerrong Road works

## Tunable Creek Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. A planned return is scheduled for 2023 to complete permanent works.



Image: Tuntable Creek Road works

## Leycester Road

Remove and replace existing material from the road surface, grade and roll the road with a temporary seal over the new surface. With a planned return to complete permanent works in 2023.



Image: Leycester Road before works

## CURRENT WORKS – DRAINAGE WORKS

### Keerrong Road

Drainage works are continuing for Keerrong Road these include desilt and reshape table drainage, while installing headwalls and pipe extensions as required to ensure water runoff from the road, to prevent future road damages from occurring.



*Image: Keerrong Road works*

## **CURRENT WORKS – RESTORATION WORKS**

### **Tunable Creek Road**

Restoration works are continuing along Tuntable Creek Road. Landslip repairs are currently underway through stabilisation works to allow rehabilitation of landslip and reinstatement of road and guardrail barrier.



*Image: Image of embankment failure before restoration works*

The photos below outline the restoration effort including works performed by a 16-tonne hydraulic crawler mounted drill rig. This remote operated machine is designed for geotechnical site investigations and is drilling around 8m into the embankment.



*Image: Images of restoration works*

## **FUTURE WORKS – SEALED ROADS**

### **Cawongla Road / Quilty Road**

All preliminary works on Cawongla Road are completed ready to commence works on the 3<sup>rd</sup> of January 2023. Quilty road has been graded and prepared for the detour route to commence on the 3<sup>rd</sup> of January 2023, vegetation trimming has been completed and drainage works have also been completed. These works have been completed with great cooperation for the public.

For further information on the works, visit the Cawongla Road update at:

[https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news\\_feed/cawongla-road-closure-for-culvert-replacement-2](https://yoursay.lismore.nsw.gov.au/maintaining-our-roads-and-bridges/news_feed/cawongla-road-closure-for-culvert-replacement-2)
